


		Nombre	Duracion	Inicio	Terminado	Predecesores	Nombres del Recurso	13 sept. 26				
								S	D	L	M	M
1		1.0 Gestión y Gobernanza	8 days	15/9/26, 8:00a. m.	24/9/26, 5:00p. m.							
2		1.1 Project Charter y Form...	3 days	15/9/26, 8:00a. m.	17/9/26, 5:00p. m.							
3		1.2 Plan de Gestión y Cron...	3 days	18/9/26, 8:00a. m.	22/9/26, 5:00p. m.	2						
4		1.3 Matriz de Riesgos y Go...	2 days	23/9/26, 8:00a. m.	24/9/26, 5:00p. m.	3						
5		2.0 Análisis de Requisitos ...	12 days	25/9/26, 8:00a. m.	12/10/26, 5:00p. m.							
6		2.1 Especificación ERS (IS...	5 days	25/9/26, 8:00a. m.	1/10/26, 5:00p. m.	4						
7		2.2 Modelado de Casos de ...	4 days	2/10/26, 8:00a. m.	7/10/26, 5:00p. m.	6						
8		2.3 Matriz de Trazabilidad d...	3 days	8/10/26, 8:00a. m.	12/10/26, 5:00p. m.	7						
9		3.0 Diseño de Arquitectur...	14 days	13/10/26, 8:00a. m.	30/10/26, 5:00p. m.							
10		3.1 Arquitectura C4 y Mod...	4 days	13/10/26, 8:00a. m.	16/10/26, 5:00p. m.	8						
11		3.2 Esquema DB Vademécu...	4 days	19/10/26, 8:00a. m.	22/10/26, 5:00p. m.	10						
12		3.3 Algoritmo Paramétrico ...	6 days	23/10/26, 8:00a. m.	30/10/26, 5:00p. m.	11						
13		4.0 Construcción Fullstac...	26 days	2/11/26, 8:00a. m.	7/12/26, 5:00p. m.							
14		4.1 Motor Backend en API ...	14 days	2/11/26, 8:00a. m.	19/11/26, 5:00p. m.	12						
15		4.2 Portal Web Clínico y G...	12 days	20/11/26, 8:00a. m.	7/12/26, 5:00p. m.	14						
16		4.3 Módulo de Recordatori...	8 days	20/11/26, 8:00a. m.	1/12/26, 5:00p. m.	14						
17		5.0 Pruebas y Control de ...	12 days	8/12/26, 8:00a. m.	23/12/26, 5:00p. m.							
18		5.1 Suite de Pruebas Auto...	5 days	8/12/26, 8:00a. m.	14/12/26, 5:00p. m.	15						
19		5.2 Pruebas de Carga, Estr...	4 days	15/12/26, 8:00a. m.	18/12/26, 5:00p. m.	18						
20		5.3 Auditoría de Seguridad...	3 days	21/12/26, 8:00a. m.	23/12/26, 5:00p. m.	19						
21		6.0 Despliegue e Implant...	8 days	24/12/26, 8:00a. m.	4/1/27, 5:00p. m.							
22		6.1 Pipeline CI/CD Automa...	3 days	24/12/26, 8:00a. m.	28/12/26, 5:00p. m.	20						
23		6.2 Pruebas Piloto de Acep...	3 days	29/12/26, 8:00a. m.	31/12/26, 5:00p. m.	22						
24		6.3 Puesta en Producción (...)	2 days	1/1/27, 8:00a. m.	4/1/27, 5:00p. m.	23						

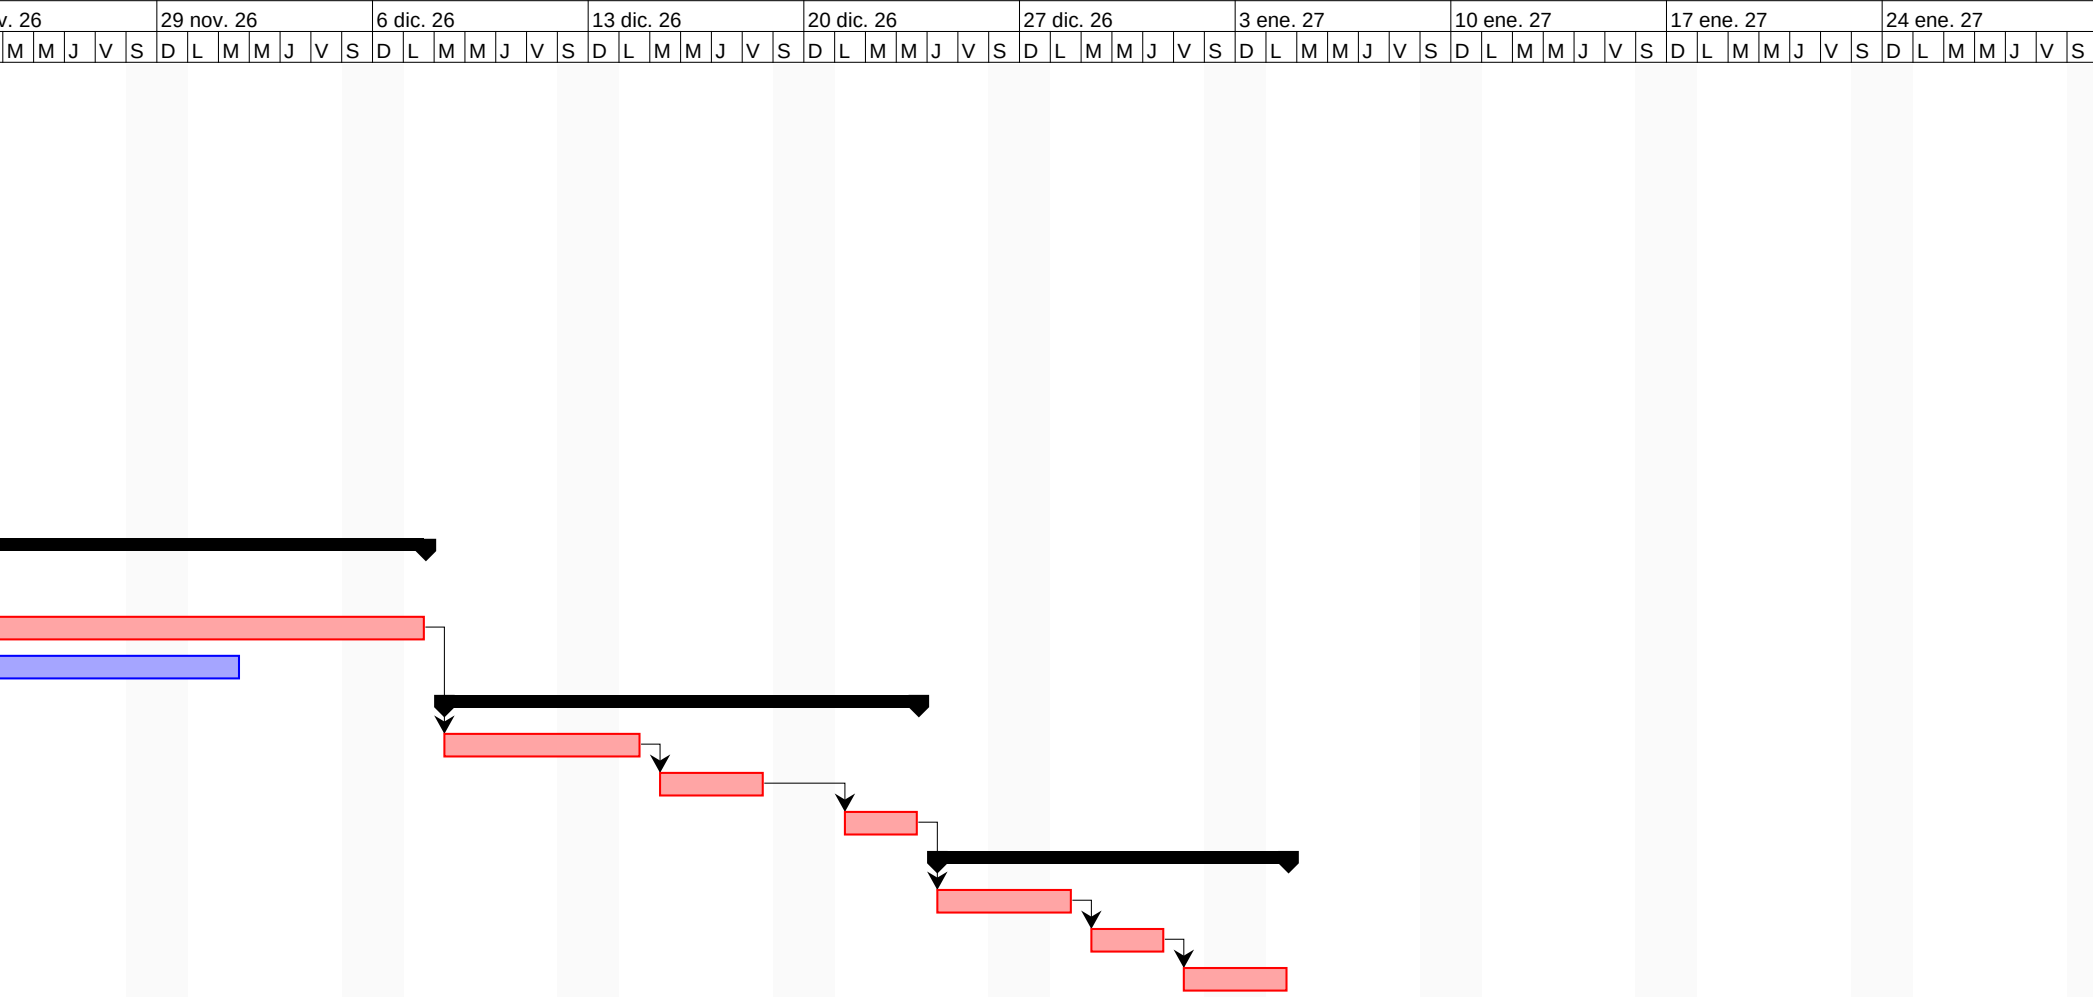

31 ene. 27			
D	L	M	M
VetDose Cl...			
